

Maintenance checks report

Checklist name	Year
MV Maintenance Year 7	7

Site	Turbine serial number	Order number
Wikinger	WK59 - 1121499	15388
Language	Revision date checklist	Approval date
en-US	5/9/2025	5/31/2025

Siemens Gamesa Renewable Energy S.A. Parque Tecnológico de Bizkaia, Edificio 222, 48170, Zamudio, Vizcaya, Spain
+34 944 03 73 52 – info@siemensgamesa.com – www.siemensgamesa.com

1. Tools

Tools				
Group	#	Name	Calibration ID	Remarks
1	1	Battery tester (Dummy-Adw020)	https://secure.elementmetech.com/MtO3/dl?x=1719D7289F88635B2G264988?2731079-1	

2. Check details

2.1. Checks from the maintenance plan

ECN				
AD 5-135_1_1_5_MV_year_null				
#	Measuring points	Remarks	Tools	Status
Location: Nacelle inside				
1	ATD000276.0: Generator - Overload clutch and bolts - Inspection			✓
2	ATD000276.1: Generator - Overload clutch body spring - Inspection			✓
3	ATD000276.2: Generator - Overload clutch mark aligned with rotor mark - Inspection	Remark 1 See annex 'Taken photos': 1		✓
4	ATD000373.0: Slip ring unit - Power bushes and rings - Inspection	Remark 1 See annex 'Taken photos': 2		✓
5	ATD000373.1: Slip ring unit - Signal bushes and rings - Inspection	Remark 1 See annex 'Taken photos': 3		✓
6	ATD000377.0: Generator - Upper grounding brush - Inspection			✓
7	ATD000377.1: Generator - Upper grounding brush support component - Inspection			✓
8	ATD000377.2: Generator - Middle grounding brush - Inspection			✓
9	ATD000377.3: Generator - Middle grounding brush support component - Inspection			✓
10	ATD000377.4: Generator - Bottom grounding brush - Inspection			✓
11	ATD000377.5: Generator - Bottom grounding brush support component - Inspection			✓
12	ATD000605.0: Generator - Enclosure of the machine and all holding fixtures - Inspection			✓
13	ATD000605.1: Generator - Stator covers seal & winding connections tightness and external damages - Inspection			✓
14	ATD000605.2: Generator - Terminal box and all the connections - Inspection			✓
15	ATD000605.3: Generator - Rotor - Inspection			✓
Location: Tower				
16	ATD000311.6: Wind turbine system - Emergency stop button at lift frame - Test			✓
17	ATD000383.0: Converter - Main components on the CCU - Inspection			✓
18	ATD000383.10: Converter - Ground connection - inspection			✓

AD 5-135_1_1_5_MV_year_null				
#	Measuring points	Remarks	Tools	Status
Location: Tower				
19	ATD000383.11: Converter - Lateral fan with heater in CCU - inspection			✓
20	ATD000383.12: Converter - Roof fan in FIU - Inspection			✓
21	ATD000383.13: Converter - Roof and door fan in POU - inspection			✓
22	ATD000383.14: Converter - Roof and door fan in DLU - inspection			✓
23	ATD000383.15: Converter - Pump - Auditory inspection			✓
24	ATD000383.16: Converter - Pump has no leakages - Inspection			✓
25	ATD000383.17: Converter - Vessel hoses - Inspection			✓
26	ATD000383.1: Converter - Cable connections on the CCU - inspection			✓
27	ATD000383.2: Converter - Main components on the FIU - Inspection			✓
28	ATD000383.3: Converter - Cable connections on the FIU - inspection			✓
29	ATD000383.4: Converter - Main components on the POU - Inspection			✓
30	ATD000383.5: Converter - Cable connections on the POU - inspection			✓
31	ATD000383.6: Converter - Main components on the DLU - Inspection			✓
32	ATD000383.7: Converter - Cable connections on the DLU - inspection			✓
33	ATD000383.8: Converter - Main components on the WCU - Inspection			✓
34	ATD000383.9: Converter - Cable connections on the WCU - inspection			✓
35	ATD000478.2: Main transformer - Oil - Sample Barcode number on bottle 5853375			✓
36	ATD000511.0: Converter cooling system - Pipe water circuit - Inspection			✓
37	ATD000538.0: Emergency lights UPS - Door fan - Auditory inspection			✓
38	ATD000538.1: Emergency lights UPS - Manual battery test - Test			✓
39	ATD000538.2: Emergency lights UPS - Fuses F4, F5, F6, F7, F8 and F9 - Inspection			✓

AD 5-135_1_1_5_MV_year_null				
#	Measuring points	Remarks	Tools	Status
Location: Tower				
40	ATD000538.3: Emergency lights UPS - All internal components and wiring - Inspection			✓
41	ATD000538.4: Emergency lights UPS - Battery box - Inspection			✓
42	ATD000538.5: Emergency lights UPS - Thermostats properly adjusted - Inspection			✓
43	ATD000538.6: Emergency lights UPS - Measurement points - Measure G1 Resistance +10.3 mOhm G1 Voltage +13.6 V G2 Resistance +9.8 mOhm G2 Voltage +13.6 V G3 Resistance +9.7 mOhm G3 Voltage +13.64 V G4 Resistance +10 mOhm G4 Voltage +13.61 V G5 Resistance +10.1 mOhm G5 Voltage +13.65 V G6 Resistance +9.8 mOhm G6 Voltage +13.63 V			✓
44	ATD000538.7: Emergency lights UPS - Tightness of all nips of each terminal and the fixed terminal adapter on the back - Inspection			✓
45	ATD000538.8: Emergency lights UPS - Filter and exhaust filter mats - Replace, if necessary			✓
46	ATD000586.0: Main UPS - Remote battery test - Test Report other tool usage Will be do by Seniortech. Battery tester No Date of the last remote battery test 31/05/2025			✓
47	ATD000586.10: Main UPS - Batteries cabinet - Inspection			✓


AD 5-135_1_1_5_MV_year_null				
#	Measuring points	Remarks	Tools	Status
Location: Tower				
48	ATD000586.1: Main UPS - Cabinet - Inspection			✓
49	ATD000586.2: Main UPS - Filter mats - Replace			✓
50	ATD000586.3: Main UPS - Manual by-pass (UPS disconnection) activation/ restarting performed? - Inspection			✓
51	ATD000586.4: Main UPS - LEDs states of rectifier and inverter - Inspection			✓
52	ATD000586.5: Main UPS - Output voltages of the rectifier - Measure Voltage in RCB +399 V			✓
53	ATD000586.6: Main UPS - Output voltages of the static by-pass - Measure Voltage in Q1 +399 V			✓
54	ATD000586.7: Main UPS - Output voltages of the inverter - Measure Voltage in OCB +397 V			✓
55	ATD000644.1: Auxiliary transformer - Earthing connections - Inspection			✓
56	ATD000644.2: Auxiliary transformer - Oil leakage - Inspection			✓
57	ATD000644.4: Auxiliary transformer - Terminal connections - Inspection			✓
58	ATD000647.0: Main transformer - Oil leakage - Inspection			✓
59	ATD000647.1: Main transformer - Paint - Inspection			✓
60	ATD000647.2: Main transformer - Earthing connection - Inspection			✓
61	ATD000647.4: Main transformer - Cooling system - Inspection			✓
62	ATD000647.5 : Main transformer - Resistance thermometer - Test Temperature difference +0 °C			✓
63	ATD000728.17: Converter - UPS batteries (2x G403 in POU) - Replace			✓
64	ATD000728.7: Converter - UPS battery (G303 in CCU) - Replace			✓

2.2. Additional checks not present in the maintenance plan

Additional tasks				
#	Measuring points	Remarks	Tools	Status
1	ATD000491.1 - Oil sample of the auxiliary transformer	Remark 1 See annex 'Taken photos': 4 Remark 2 Iso 3 Nr.5853387		✓

3. Annexes


3.1. Taken photos

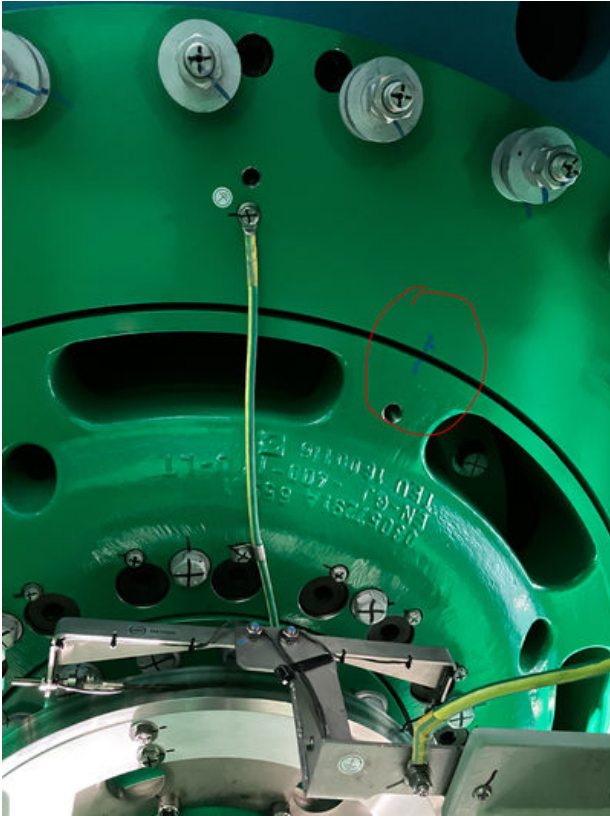

1 Figure from Checklist 'AD 5-135_1_1_5_MV_year_null', Task 3 - Remarks



2 Figure from Checklist 'AD 5-135_1_1_5_MV_year_null', Task 4 - Remarks

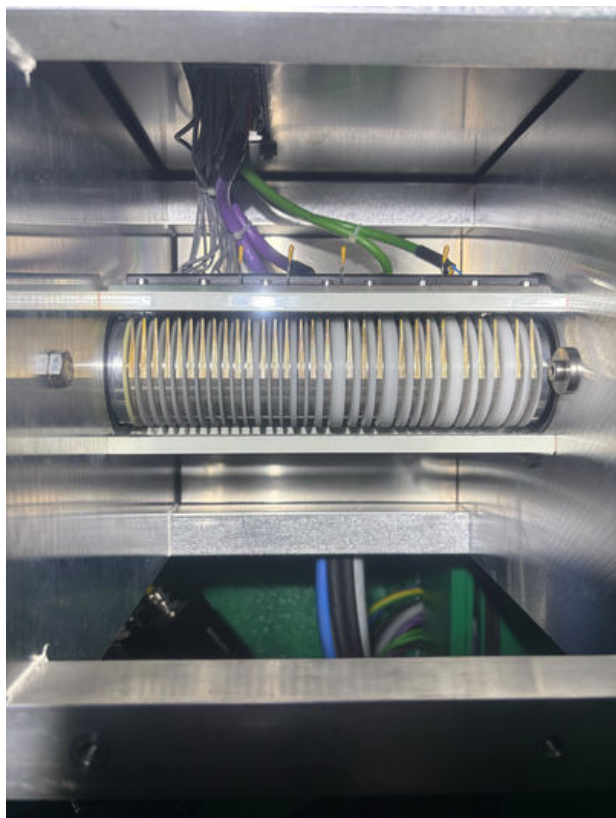

3 Figure from Checklist 'AD 5-135_1_1_5_MV_year_null', Task 5 - Remarks



4 Figure from undefined, Task 1 - Remarks
